# **I-280 Soundwalls Project**

RFP S19199 Pre-Proposal Conference Project Overview

October 29, 2019



### Outline

Project Overview

RFP Scope of Services


Schedule





# **Project Overview**

- Project limits on I-280 from SR 87 to Los Gatos Creek
- 5 walls (8–16 feet tall)
- Approx. 3900 total linear feet of soundwall
- Previous reports
  - NBSSR (1992)
  - Noise Reduction Screening Program (2011)

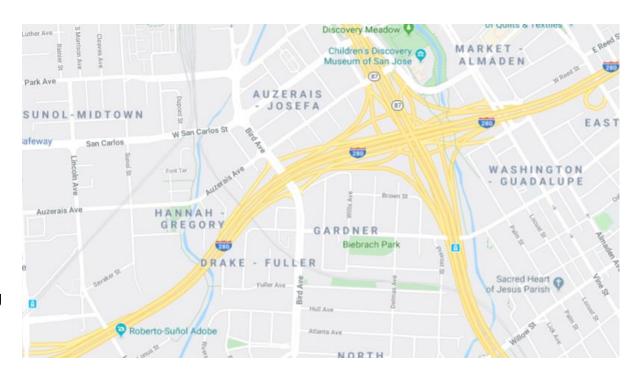



**Proposed Soundwall Locations** 





**Proposed Soundwall Locations** 





## RFP Scope of Services

#### PA/ED

- Environmental Studies
  - Noise Study
  - Visual Impact
- Conceptual Layout
  - Walls on creek bridge
- Environmental Clearance
- Public Outreach Support
- Project Report

- Coordination
  - Caltrans
  - City of San Jose
- Optional Services through amendments
  - PS&E/ROW
  - Design Support During Construction



#### Schedule

#### Preliminary Project Milestone Schedule

Activity	Early Start	Early Finish	2019	2020	2021	2022	2023	2024	2025
RFP Process	Sep-2019	Jan-2020							
Project Approval/Environmental Document (PA/ED)	Jan-2020	May-2021							
Complete PA/ED		May-2021			•				
Final Design - Plans, Specification, Plans (PS&E) (1)	May-2021	Dec-2022							
Right-of-Way (ROW) <sup>(1)</sup>	Oct-2021	Dec-2022							
Complete PS&E & ROW		Jun-2022				•			
Construction <sup>(2)</sup>	Jan-2023	Jun-2025							
Open to Traffic		Jun-2025							•
Closeout	Jul-2025	Apr-2026							

